



School Building Infrastructure & Project Management Stewardship Report



Prepared By:
Frank Fanelli, Director of Project Management

August 10, 2023

STRATEGIC PLAN : SY 2020-2024



NEW HAVEN PUBLIC SCHOOLS

Core Values

We believe...

- 1 Equitable opportunities** create the foundation necessary for every child to succeed
- 2 A culture of continuous improvement** will ensure that all staff are learners and reflective practitioners
- 3 High expectations** and standards are necessary to prepare students for college and career
- 4 Collaboration** and partnerships with families and the New Haven community will enhance learning and achievement



Mission

To provide all students in New Haven Public Schools with personalized, authentic, and engaging learning experiences through creativity, exploration, innovation, critical thinking, problem-solving, and high quality instruction. To foster a culture of continuous improvement through collaborative partnerships with staff, families, and the New Haven community. To support students' growth and development by utilizing the Whole Child Framework.

Vision

Our vision is to be a premier urban school district that ensures access to equitable opportunities and successful outcomes for all students as they prepare for college, career, and life.

Priority Areas for 2020-2024

- | | |
|------------------------------------|-----------------------------|
| 1 Academic Learning | 2 Culture & Climate |
| 3 Youth & Family Engagement | 4 Talented Educators |
| 5 Operational Efficiencies | |










School Life Safety & Security Systems







Project Planning & Status Worksheet 1 of 2



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District Schools
Project Name :	Fire Panel Replacement
Project Assigned to :	Director of Project Management / Facilities

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		










Task	School	Status	Comments
Panel obsolete,	Hillhouse		<ul style="list-style-type: none"> Waiting for quote, immediate replacement is needed.
Panel obsolete, opposed upgrade to Edward EST4	Davis Street		<ul style="list-style-type: none"> Partnering with IES to design a new System
Panel obsolete, opposed upgrade to Edward EST4	Lincoln Basset		<ul style="list-style-type: none"> Partnering with IES to design a new System
Panel obsolete, opposed upgrade to Edward EST4	Edgewood		<ul style="list-style-type: none"> Partnering with IES to design a new System
Panel obsolete, opposed upgrade to Edward EST4	Hooker Middle		<ul style="list-style-type: none"> Partnering with IES to design a new System
Panel obsolete, opposed upgrade to Edward EST4	King Robinson		<ul style="list-style-type: none"> Partnering with IES to design a new System




Project Planning & Status Worksheet 1 of 2



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District Schools
Project Name :	Door Repairs / Replacement
Project Assigned to :	Facilities, Carpenter & Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		










Task	School	Status	Comments
Replace front doors	Brennen Rogers		<ul style="list-style-type: none"> Builders Hardware is working on a quote to replace the 4 main entrance doors
Assessment of exterior doors	Hillhouse		<ul style="list-style-type: none"> Director of PM met with Builders Hardware to determine doors that need imminent replacement Received quote to replace damaged doors Bid document need to be created
Interior Doors	Cross		<ul style="list-style-type: none"> Builders Hardware is evaluating the interior doors for possible total replacement or hardware replacement








Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District Schools
Project Name :	Clock Bell & PA Systems Repairs / Replacement
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		










Task	Status	Comments
Hillhouse		<ul style="list-style-type: none"> Consolidated Electric has the PO's.... Materials are on order
Cross		<ul style="list-style-type: none"> Consolidated Electric has the PO's.... Materials are on order
Metro		<ul style="list-style-type: none"> Consolidated Electric has the PO's.... Materials are on order
Troup		<ul style="list-style-type: none"> Need full replacement Approved by F&O Aug 7
Brennen Rogers		<ul style="list-style-type: none"> Need full replacement Approved by F&O Aug 7
Mauro Sharden		<ul style="list-style-type: none"> Need full replacement Approved by F&O Aug 7
Ross Woodward		<ul style="list-style-type: none"> Need full replacement Approved by F&O Aug 7





Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Electronic Access Control
Project Assigned to :	IT, Security & Facilities

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

Task	Status	Comments
New Haven Academy <ul style="list-style-type: none"> 70 Card door readers and associated hardware 		<ul style="list-style-type: none"> School Security Grant Enhancements Phase 5 PO issued, waiting on parts (parts backordered) Director of PM needs to have a planning meeting with IT
Mayo <ul style="list-style-type: none"> 79 Card door readers and associated hardware 		<ul style="list-style-type: none"> School Security Grant Enhancements Phase 5 PO issued, waiting on parts (parts backordered) Director of PM needs to have a planning meeting with IT
ESUMS <ul style="list-style-type: none"> Replacing cameras, card readers and other related equipment 		<ul style="list-style-type: none"> Waiting on PO to be issued Director of PM needs to have a planning meeting with IT
Edgewood <ul style="list-style-type: none"> Replacing cameras, card readers and other related equipment 		<ul style="list-style-type: none"> PO issued Feb. 21, 23 Director of PM needs to have a planning meeting with IT

Project Planning & Status Worksheet 1 of 2



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :

NHPS District

Project Name :

Long Term Facilities Plan

Project Assigned to :

COO Office



In Progress

Delayed

Stopped

Completed

On Going

Material on Order

Awaiting Contract Approval from Corporation Council

Awaiting Approval F&O / BOE / BOA

Waiting on Others

Task	Status	Comments
School Building capacity surveys requested from Principals	Completed	<ul style="list-style-type: none"> All have been completed and received by Svigals
MEP Condition Assessments	Completed	<ul style="list-style-type: none"> Building assessments have been completed in coordination with Facilities Staff and data collected for inclusion in the Facilities Master Plan.
Development of Recommendations	In Progress	<ul style="list-style-type: none"> Tom Lamb and Svigals will be presenting to the BOE on June 26.










State of Connecticut School Construction Projects


Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	School Construction Program
Project Name :	State Construction Project Audits
Project Assigned to :	COO Office

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

Task	Status	Comments
Projects next for State Audit		<ol style="list-style-type: none"> Roberto Clemente Hill Central Bowen Field <p>Not scheduled with the State yet. No New Information from the State of CT</p> <p>Meeting held with new Director of School Construction at the state to review open audits. Scheduling of Audits no longer is done by the office of School construction. They are completed by DAS.</p>

Energy Management & Sustainability

Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :

District Wide

Project Name :

Future LED Lighting Program

Project Assigned to :

Director of Project Management



In Progress
Delayed
Stopped
Completed



On Going
Material on Order
Awaiting Contract Approval from Corporation Council
Awaiting Approval F&O / BOE / BOA



Waiting on Others
Out for RFQ/RFI/RFP/Bid

Task	Status	Comments
Davis Street		<ul style="list-style-type: none"> waiting for plans from IES on design
Martinez		<ul style="list-style-type: none"> waiting for plans from IES on design
Cross		<ul style="list-style-type: none"> waiting for plans from IES on design
Hillhouse		<ul style="list-style-type: none"> waiting for plans from IES on design
Brennen		<ul style="list-style-type: none"> waiting for plans from IES on design
Conte		<ul style="list-style-type: none"> waiting for plans from IES on design

Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :

District Wide

Project Name :

Currant LED Lighting Program

Project Assigned to :

Facilities Team



In Progress
Delayed
Stopped
Completed



On Going
Material on Order
Awaiting Contract Approval from Corporation Council
Awaiting Approval F&O / BOE / BOA




Waiting on Others
Out for RFQ/RFI/RFP/Bid

Task	Status	Comments
Clinton Ave School LED Retrofit		
Troup School LED Retrofit	75% Completed	<ul style="list-style-type: none"> All exterior is completed Interior will be completed by Aug 25, 2023
Metro Business Academy LED Retrofit	90% Completed	<ul style="list-style-type: none"> N Power has completed all but the exterior
Career High School LED Retrofit		

Clinton Ave School Before & After

LED Upgrade

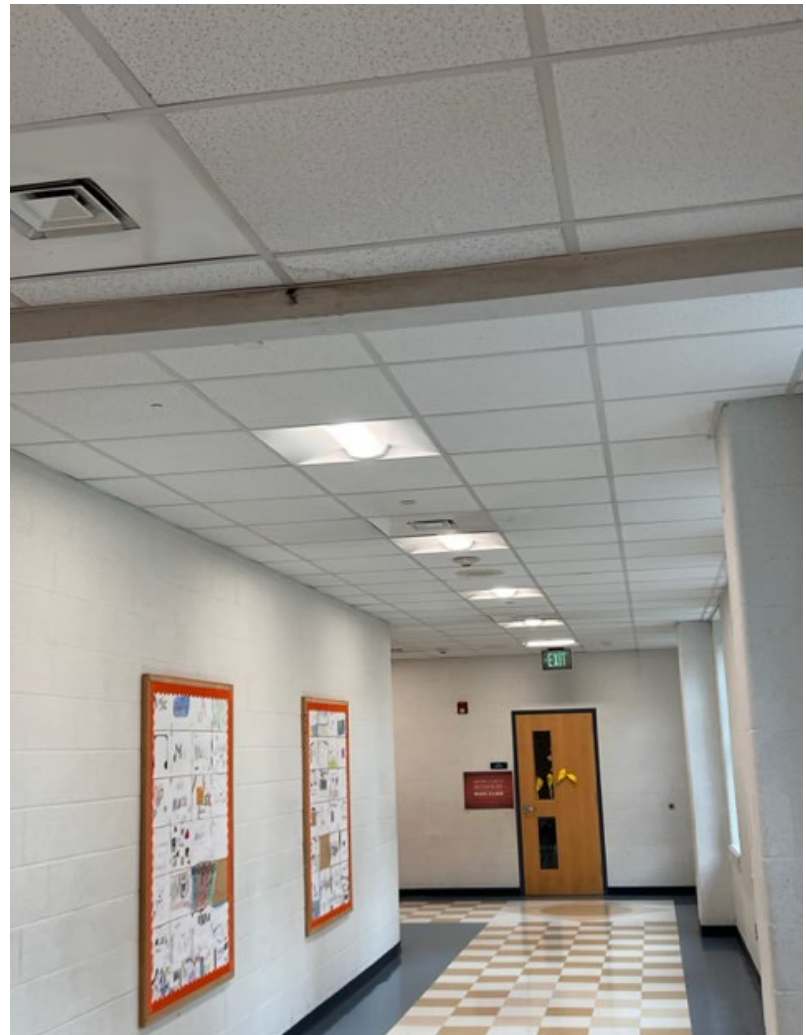

Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :

All Schools

Project Name :

Building Management System Upgrades to Honeywell Tridium

Project Assigned to :

Facilities Team, COO Office



In Progress
Delayed
Stopped
Completed



On Going
Material on Order
Awaiting Contract Approval from Corporation Council
Awaiting Approval F&O / BOE / BOA



Waiting on Others
Out for RFQ/RFI/RFP/Bid











Task	Status	Comments
Mauro Sheridan		<ul style="list-style-type: none"> EBI Servers need to be upgraded to Tridium RFP to be written by Facilities Director and Facilities HVAC Manager
Fair Haven		<ul style="list-style-type: none"> EBI Servers need to be upgraded to Tridium RFP to be written by Facilities Director and Facilities HVAC Manager
Jepson		<ul style="list-style-type: none"> EBI Servers need to be upgraded to Tridium RFP to be written by Facilities Director and Facilities HVAC Manager
Kathrin Brennan		<ul style="list-style-type: none"> EBI Servers need to be upgraded to Tridium RFP to be written by Facilities Director and Facilities HVAC Manager








Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Domestic Hot Water Boilers
Project Assigned to :	Director of Project Management / Facilities Team

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		











School	Status	Comments
Mauro Sheridan		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design
Clinton Ave		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design
Davis Street		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design
Edgewood		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design
Fair Haven		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design
FAME		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design
Conte		<ul style="list-style-type: none"> Tank is actively leaking, past life expectancy. Routolo recommends immediate replacement waiting for plans from IES on design .

Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	All Schools
Project Name :	Heating Boiler Replacements & Upgrades
Project Assigned to :	Director of Project Management / Facilities HVAC Manager

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

Task	Status	Comments
Hillhouse	25% completed	<ul style="list-style-type: none"> Demo has been completed Boilers were ordered, due in by end of Aug, 2023
Wilber Cross	99% completed	<ul style="list-style-type: none"> Commissioning is scheduled for Aug 11.
Nathen Hale		<ul style="list-style-type: none"> Waiting on plans from IES on design
Ross Woodward		<ul style="list-style-type: none"> Waiting on plans from IES on design
Lincoln Basset		<ul style="list-style-type: none"> Waiting on plans from IES on design
Clarence Rogers		<ul style="list-style-type: none"> Waiting on plans from IES on design
Daniels		<ul style="list-style-type: none"> Waiting on plans from IES on design

Cross Heating Boiler Replacements & Upgrades


















Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Building HVAC System Repair & Replace
Project Assigned to :	Director of Project Management / Facilities HVAC Manager

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		











Task	Status	Comments
Beecher		<ul style="list-style-type: none"> Temp Chiller was installed the last week in June 2023 Bid is currently open for Chiller replacement, pre bid meeting is Aug 14
Hillhouse		<ul style="list-style-type: none"> Replacement of water tower and chiller was installed Both chillers need to be rebuilt waiting on quotes Meeting with Tucker Aug 15 to discuss scope
Martinez		<ul style="list-style-type: none"> Temp Chiller was installed the last week in June 2023 Bid will go live Aug 20
Cross		<ul style="list-style-type: none"> Building is currently stay cool Chiller requires montane to stay functioning properly... Tucker is currently working to fix all issue
Clinton Ave		<ul style="list-style-type: none"> Design is complete Bid will go live Aug 20






Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Building HVAC System Repair & Replace
Project Assigned to :	Director of Project Management / Facilities HVAC Manager

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		











Task	Status	Comments
Clarence Rogers		<ul style="list-style-type: none"> One chiller is currently running As of now school is functioning properly
Fairhaven		<ul style="list-style-type: none"> Currently 2 units are down, CT Controls is working on the server to fix the issue.
Nathan Hale		<ul style="list-style-type: none"> Every Unit is function efficiently
Clemente/ Hill Central		<ul style="list-style-type: none"> Every Unit is function efficiently
New Haven Academy		<ul style="list-style-type: none"> Every Unit is function efficiently





Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Building HVAC System Repair & Replace
Project Assigned to :	Director of Project Management / Facilities HVAC Manager

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

Task	Status	Comments
Obama		<ul style="list-style-type: none"> Every Unit is function efficiently
HSC		<ul style="list-style-type: none"> Currently roof top 8 has control issue. CT Controls is currently working to resolve the issue
Edgewood		<ul style="list-style-type: none"> Every Unit is function efficiently
		










School Infrastructure Project Planning







Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Roof Replacements
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped	Awaiting Contract Approval from Corporation Council			
	Completed		Awaiting Approval F&O / BOE / BOA		











Task	Status	Comments
Conte • Main office roof replacement		Completed
Hillhouse • Auditorium roof (only) replacement		<ul style="list-style-type: none"> Barrett Construction was awarded Demo is starting Aug 21
Hillhouse • Total roof replacement		<ul style="list-style-type: none"> Waiting for quote
Fairhaven		<ul style="list-style-type: none"> Waiting for quote
Conte • Total roof replacement		<ul style="list-style-type: none"> Waiting for quote
HSC		<ul style="list-style-type: none"> Waiting for quote



Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Adult Ed
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		Out for RFQ/RFI/RFP/Bid
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

Task	Status	Comments
New Adult Ed location determined		<ul style="list-style-type: none"> 188 Bassett St New Haven
Adult Ed		<ul style="list-style-type: none"> Bid for Architect went live Sunday July 23

Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	Wooster Place
Project Name :	Department Head offices
Project Assigned to :	Director of Project Management



In Progress
Delayed
Stopped
Completed



On Going

Material on Order

Awaiting Contract Approval from Corporation Council

Awaiting Approval F&O / BOE / BOA



Waiting on Others

Out for RFQ/RFI/RFP/Bid










Task	Status	Comments
Abetment	Completed	<ul style="list-style-type: none"> Work completed by Yankee construction
Architectural drawings and design	Completed	<ul style="list-style-type: none"> Work completed by Svigals Architectural Services
Interior construction	Awaiting Approval F&O / BOE / BOA	<ul style="list-style-type: none"> Project was awarded to Prete Construction F&O approved Aug 7




Project Planning & Status Worksheet 1 of 2



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Swimming Pool Maintenance & Repairs
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		










Task	Status	Comments
Career School		<ul style="list-style-type: none"> IES working on drawing design for new Dehumidification
Conte School <ul style="list-style-type: none"> Pool was inspected by engineering firm for cracks in foundation. Pool leaking into mechanical space under pool. Pool liner recommended Filter sand media needs to be replaced 		<ul style="list-style-type: none"> Bid was awarded to CT Custom Aquatic's Waiting on PO
Cross		<ul style="list-style-type: none"> Temporarily closed due to ceiling tiles and ceiling grid damage Roof was evaluated for total replacement Working with IES and Svigals on Designs IES is working on the dehumidification replacement Svigals is working on design of ceiling and pool Surroundings



Project Planning & Status Worksheet 1 of 2



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Swimming Pool Maintenance & Repairs
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

Task	Status	Comments
Hillhouse <ul style="list-style-type: none"> Multiple upgrades needed to keep pool open... Main Drain, Controller replacement, Chemical Feed System, Tile repair, Balancing 		<ul style="list-style-type: none"> Finished
Martinez <ul style="list-style-type: none"> Dehumidification Replacement 		<ul style="list-style-type: none"> Contract Awarded to Pro-Mech. Inc Demo is complete Painting is complete Ductwork will starting being installed by the end of Aug. 2023 Looking to install unit around the last week of Oct. 2023 Tentative pool open date is January 2024

Martinez

















Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Playgrounds Inspection Maintenance & Repair
Project Assigned to :	Facilities

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

School	Status	Task / Comments
Edgewood <ul style="list-style-type: none"> Entire playground upgrade/redesign Problems with, tree root, Flooding and drainage 		<ul style="list-style-type: none"> RFP to be written and requested to go live by first week of August Funding approved.... ESSER Funds
Truman/Head Start		<ul style="list-style-type: none"> Finished
Fair Haven/Head Start		<ul style="list-style-type: none"> Awarded to O'Brian & Son Design was approved by Frank Fanelli Install starting after August 15, 2023 Will be completed before the start of the new school year
Lincoln-Bassett/Head Start		<ul style="list-style-type: none"> Finished
Brennan Rogers		<ul style="list-style-type: none"> New Playground is being added Waiting for quote from O'Brian & Sons Funding Source ESSER

HeadStart Playground Remodel

Lincoln Bassett



Truman
















Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	FLAC
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

School	Status	Task / Comments
FLAC Bleachers		<ul style="list-style-type: none"> Bleacher Need total replacement Bleacher are 22 years old and are in disrepair.
FLAC Indoor Track		<ul style="list-style-type: none"> Interior Track need total replacement Track in 10 years old with no warranty Last replacement the track was installed over the original. Causing moisture buildup that is bubbling and making the surface unsafe Director of PM has worked with many contractors and engineers to obtain quote for replacement
FLAC Hallway		<ul style="list-style-type: none"> Long hall between FLAC and Hillhouse is bubbling up Per multiple reps the material used was not appropriately installed to withstand the roughness from the spicks on cleats. Director of PM has worked with many companies to find a highly resistant wearable replacement. All quotes include install, demo & disposing of old product along with a 10 year warranty
		

Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Sanitary Napkin Dispensers
Project Assigned to :	Director of Project Management



In Progress
Delayed
Stopped
Completed



On Going
Material on Order
Awaiting Contract Approval from Corporation Council
Awaiting Approval F&O / BOE / BOA



Waiting on Others










School	Status	Task / Comments
Install district wide		<ul style="list-style-type: none"> Per The State of CT unfunded mandate (passed in legislation this year) Sanitary Napkin Dispensers must be installed in every female restroom through out the district, along with 1 male restroom in every building. Director of PM to write RFP




Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	School Based Clinics
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		










School	Status	Task / Comments
Metro <ul style="list-style-type: none"> Add new SBHC to location 		<ul style="list-style-type: none"> Requested Svigals to start deign Director of PM along with Svigals Architects meet with Sue Petters & Paula Sutton to discuss details of the install Waiting on grant funding
Ross Woodward		<ul style="list-style-type: none"> Funding approved Design is compete Bid going live August 20, 2023
Mauro Sheriden		<ul style="list-style-type: none"> New reception deck needs to be order.




Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Science Labs
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		










School	Status	Task / Comments
Hillhouse		<ul style="list-style-type: none"> Director of PM met with Bob McCain, Keisha Hannans, and Svigals Architect to start Planning the design. Phase one each school will have 1 lab full remodeled and upgraded. Phase 2 all labs in the school will be full remodeled and upgraded Svigals Architect are in the design development phase
Cross		<ul style="list-style-type: none"> Director of PM met with Bob McCain, Keisha Hannans, and Svigals Architect to start Planning the design. Phase one each school will have 1 lab full remodeled and upgraded. Phase 2 all labs in the school will be full remodeled and upgraded Svigals Architect are in the design development phase
Sound		<ul style="list-style-type: none"> Director of PM met with Bob McCain, Keisha Hannans, and Svigals Architect to start Planning the design. Phase one each school will have 1 lab full remodeled and upgraded. Phase 2 all labs in the school will be full remodeled and upgraded Svigals Architect are in the design development phase



Project Planning & Status Worksheet



NEW HAVEN PUBLIC SCHOOLS

School Name / Program / Building :	District
Project Name :	Manufacturing Program
Project Assigned to :	Director of Project Management

	In Progress		On Going		Waiting on Others
	Delayed		Material on Order		
	Stopped		Awaiting Contract Approval from Corporation Council		
	Completed		Awaiting Approval F&O / BOE / BOA		

School	Status	Task / Comments
Hillhouse		<ul style="list-style-type: none"> NHPS was awarded a grant to add Manufacturing classrooms to Hillhouse Chris Williams Architect was awarded the contract Plans have been completed Bid going live August 20, 2023
Cross		<ul style="list-style-type: none"> NHPS was awarded a grant to add Manufacturing classrooms to Cross Chris Williams Architect was awarded the contract Plans have been completed Bid going live August 20, 2023
	
